

Thirty seven ways this could go wrong

Six domains, thirty seven scored scenarios, and a response written against a dated milestone or a published figure in every one. Every number traces to the master pro forma of 16 August 2026 and every external claim opens in one click. Six scenarios score the maximum, and they reduce to three facts.

01	Regulatory and Policy	6 scenarios
02	Competitive	7 scenarios
03	Customer Adoption and Timing	6 scenarios
04	Execution and Platform	6 scenarios
05	Funding and Runway	6 scenarios
06	Key-Person and Team	6 scenarios

EXECUTIVE OVERVIEW · HOW TO READ THE BUNDLE

Six domains, and where the weight sits

Each domain is a separate document. Every scenario is scored on likelihood and impact from 1 to 3 into a score out of 9, paired with either a company that lived through a structurally similar failure or a figure from the plan itself, and answered with a response written against a dated milestone. **Every scenario also carries an early warning signal, which is the thing that can be observed before the scenario arrives.** Those signals are the lines worth putting on a board agenda. The scenarios themselves are context for them.

37

SCENARIOS
ACROSS SIX
DOMAINS

6

SCORE THE
MAXIMUM OF NINE

3

FACTS BEHIND
ALL SIX OF THOSE


0

PAYING CUSTOMERS
AS AT AUGUST 2026

745

FIRMS IN THE
FIRST POPULATION

SCENARIOS BY BAND, DOMAIN BY DOMAIN

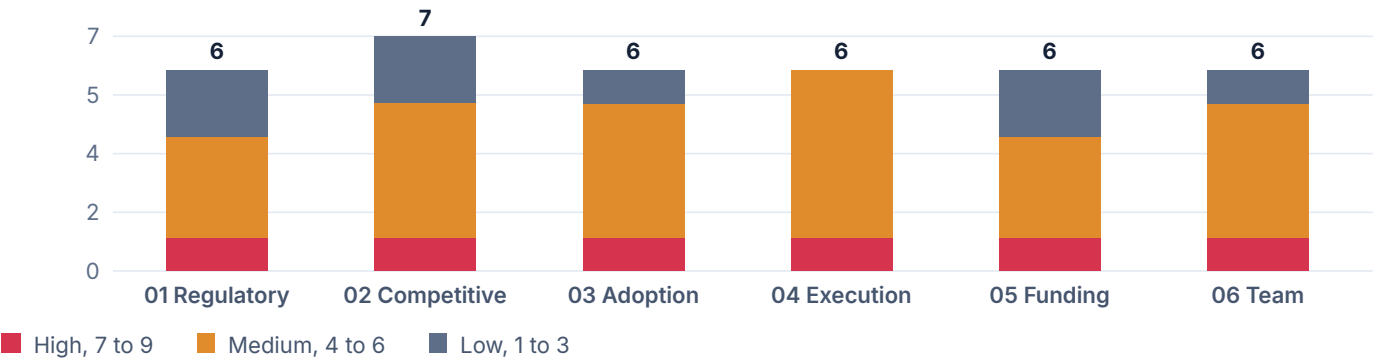

Bars start at zero and run to seven, the largest domain. Exactly one scenario in each domain scores the maximum. Source: the six domain documents in this bundle.

SOURCES ON THIS PAGE

Scoring	Likelihood and impact are management judgements on a 1 to 3 scale, made against the figures in 4orm Finance master pro forma rebuild of 16 August 2026, base case, recalculated in full and the vendor material assessed in 4orm Finance Comparables and Benchmarks, 17 August 2026.	MODEL
Position as at August 2026	No paying customers, no signed contracts, two design partners in prospect, three people employed. 4orm Finance master pro forma rebuild of 16 August 2026, base case, recalculated in full, cohorts and team roadmap tabs.	MODEL

Six scenarios score the maximum, and they reduce to three facts

The six are listed first, then the three facts underneath them. The control column names the cheapest thing that moves each scenario rather than everything that would help, because a register whose every line needs a project is a register nobody re-runs.

Scenario	Domain	The single most useful control
The forcing event has no date in law	01 Regulatory	Sell the daily ledger and the 31 March return, both already in force. Never quote 8 September 2028 as a deadline
AutoRek productises Canada without announcing it	02 Competitive	Its own website, checked every quarter. Three signed enterprise contracts and one accepted review pack before the seed is priced
970 signatures are required and none has happened	03 Adoption	Signatures counted monthly against the annual plan, with the channel share as the lever rather than the price
A thing that cannot be added later is traded for a date	04 Execution	All four in the architecture note that gates the money, each one demonstrated running rather than described
The road is overdrawn in eight months	05 Funding	The cut list and the facility decision written down before February 2027, and runway reported in months every board update
Three people own it and seventy nine contracted people deliver it	06 Team	Every partner scope checked against the permission table before it is signed, and a named backup reviewer on architecture acceptance

Legend. One scenario from each domain. The control column names the cheapest thing that moves the scenario, not everything that would help.

SOURCES ON THIS PAGE

The top tier	One scenario from each of the six domain documents in this bundle, each scored likelihood 3 by impact 3.	MODEL
Section 17	A review at least once every three years, with no first date and no period the review must cover. Justice Laws Canada · reviewer independence	PRIMARY
The road	Lowest month \$778,960 short in May 2028, eight months overdrawn, narrowing to \$340,891 across five months with the facility drawn. 4orm Finance master pro forma rebuild of 16 August 2026, base case, recalculated in full, map to seed tab, and 4orm Finance Vision, 17 August 2026 section 13.	MODEL

1

Nothing has been sold yet

- 970 signatures across five years and eight overdrawn months are the same fact from two sides: cost arrives before revenue does.
- The lowest month is May 2028 at a shortfall of \$778,960, and the borrowing facility narrows it to \$340,891 across five months without closing it.
- Both are fixed by the same three levers, and all three have to be decided before February 2027 rather than in it.

2

The urgency is real, the date is not

- The daily ledger duty and the 31 March return are both in force and both checkable in one click.
- Section 17 names no first review date and no period a review must cover, so the pressure the pitch leans on has to come from the duty itself.
- The competitive window is the same shape: real, open now, and nobody's to set the length of.

3

The defensible part is cheap and invisible

- The four things that cannot be added to the record later cost days or weeks in the first release.
- The separations that make a record evidence cost almost nothing at three people and a great deal to reinstate at forty seven.
- None of it shows in a demonstration, which is why it is the work that gets traded for a date.

Six scenarios score the maximum and none of them is a surprise to the plan that produced them.

Each of the three facts above appears in the plan's own documents before it appears here. The eight overdrawn months, the statutory position on section 17, and the four things that cannot be added later are all published rather than found. A register attacked only from the outside would read very differently, and it would be wrong in more places.

HOW TO READ ONE SCENARIO

The score	Likelihood 1 to 3 multiplied by impact 1 to 3. High is 7 to 9, medium 4 to 6, low 1 to 3, and the bubble is sized by the product.
The trigger and the signal	What has to happen for the scenario to be live, and the observable thing that comes first. Every signal is either a figure in the model, a line in a document, or something on somebody else's website.
The evidence and the response	Either a named company that lived through a structurally similar failure, with its own filings cited, or a figure from the plan with its tab named. The response is written against a dated milestone, a signature or a figure, never against a principle.
The cadence	The last page of each document, and the only page that has to be read on a schedule.

SOURCES ON THIS PAGE

The three facts	Each appears in the plan's own documents before it appears here. 4orm Finance Vision, 17 August 2026, section 12 · 4orm Finance master pro forma rebuild of 16 August 2026, base case, recalculated in full, checks and map to seed tabs · 4orm Finance Technical Architecture 03.2, 17 August 2026, the four things that have to be right in the first release.	MODEL
-----------------	--	-------

One calendar, and every matrix keys off it

When a date on this list moves, re-run every matrix that references it. The tranche gates, the design partner chain and the month by month road are the load-bearing structure underneath all six domains. The list runs to the seed and stops there, because nothing in this bundle is scored against a date beyond it.

When	What kind	What has to be true
Q3 2026	Capital and product	\$550,000 in the account from the two subscription agreements. Architecture note delivered and accepted, tested against the four properties. Intellectual property assignment signed, before any deposit moves.
Q4 2026	Commercial and capital	Twenty discovery calls off the published register. Two design partners scoped, signed and scheduled. First open instalment of \$500,000 released against all four.
Feb 2027	Cash	The first overdrawn month on the road, at \$40,667 short. The cut list and the facility decision have to exist before this month, not during it.
Q1 2027	Commercial and capital	Both design partners live in production, which is a different milestone from signed. First paying subscription customer at list price. Second open instalment of \$500,000.
Q2 2027	Product and capital	The automated test proving an old export can be reproduced exactly, running on every build. \$10,000 a month of recurring revenue across at least five customers. Third open instalment of \$500,000.
Q4 2027	Product	Full duty set shipped: framework, testing, incidents, changes and the 31 March return, on one engine.

Legend. August 2026 to the end of 2027. Source: 4orm Finance master pro forma rebuild of 16 August 2026, base case, recalculated in full, milestones, capital structure and map to seed tabs.

SOURCES ON THIS PAGE

The duty and its start	Safeguarding frameworks have applied to relevant payment service providers since 8 September 2025, and the annual report is due 31 March each year. Bank of Canada · annual reporting · the safeguarding guideline	PRIMARY
What the regulation names	Section 15, the daily per end user ledger. Section 17, a review at least once every three years, with no first date and no period it must cover. Section 18, the annual report. Justice Laws Canada · reviewer independence	PRIMARY
The eighteen milestones	Product, regulatory, commercial, legal and financial, each one either true or not, with the status column the only editable cells on the tab. 4orm Finance master pro forma rebuild of 16 August 2026, base case, recalculated in full, milestones tab.	MODEL

The calendar, continued into 2028

The last entry is on the list specifically so that it is never mistaken for one of the others. Everything above it is a milestone or a month. It is neither.

When	What kind	What has to be true
1 Jan 2028	Price	The card steps for the last time, to 1.25, and holds there for the rest of the plan. A firm keeps the price it signed at, so the 2027 column is a closing price rather than a discount.
Q1 2028	Commercial	Ten paying, deployed, reference-able customers. The milestone the whole plan turns on. Not revenue, not pipeline, not letters of intent.
Feb to Aug 2028	Cash	Seven consecutive overdrawn months, the lowest being May 2028 at \$778,960 short. This is the reason the pre-seed is sized where it is.
Q2 2028	Regulatory	First outside review passed on our own export, accepted without a follow up request, on the first attempt.
Q3 2028	Product and commercial	Second rule maker configured with no second version of the software, which is the platform claim tested rather than argued. Days to first value under two weeks by customer twenty.
8 Sept 2028	Arithmetic, not a deadline	Three years from the day the safeguarding duty commenced. The regulation names no first review date and imposes no period a review must cover, so this date is offered as arithmetic and appears nowhere in this bundle as a due date.
Q4 2028	Capital	Seed round closed on evidence rather than on a deck: \$3,500,000 at \$30,000,000 post-money, 1.54 times the recurring revenue at the end of 2028.

Legend. Every date above is a milestone from the master pro forma or a month from the twenty nine month road, except the last, which is arithmetic from 8 September 2025 and is labelled as arithmetic. Source: 4orm Finance master pro forma rebuild of 16 August 2026, base case, recalculated in full, milestones, capital structure and map to seed tabs.

SOURCES ON THIS PAGE

The duty and its start	Safeguarding frameworks have applied to relevant payment service providers since 8 September 2025. The annual report is due 31 March each year. Bank of Canada · annual reporting	PRIMARY
What the regulation names	Section 15, the daily per end user ledger. Section 17, a review at least once every three years, with no first date and no period it must cover. Section 18, the annual report. Justice Laws Canada · reviewer independence	PRIMARY
The eighteen milestones	Product, regulatory, commercial, legal and financial, each one either true or not, with the status column the only editable cells on the tab. 4orm Finance master pro forma rebuild of 16 August 2026, base case, recalculated in full, milestones tab.	MODEL

Every figure in this bundle traces to one workbook, and the workbook checks itself in sixty five places.

Two of those checks read REVIEW by design and both are in the funding domain. Nine switches turn whole parts of the plan off so a reader can test it rather than argue about it, and the answer to which assumption the plan leans on hardest is printed in this bundle rather than left to be found: it is the research credits, worth \$2,351,025 across the plan, and removing them doubles the overdrawn months from eight to sixteen.

The figures every matrix is scored against

One number, one place. Every scenario in the six documents is scored against this list, and any figure not on it or derived from it does not appear.

The register	18,254 entities across five mutually exclusive tiers and eleven industries. 13 of 32 rows primary sourced, 18 of 31 management estimates.
The first population	745 registered payment service providers that hold end user funds, of 1,562 registered, with 459 in review held outside the denominator. The duty attaches to holding the money rather than to being registered.
Capture	214 firms by 2031, which is 28.7 per cent of 745. About 60 firms, 8.1 per cent, three years after the duty commenced. Blended capture of 4.7 per cent across the whole register exists so the arithmetic ties and is never published.
The card, held flat	\$687,000 command and institution, \$219,500 enterprise and complex, \$83,250 mid market, \$29,450 small regulated firm, \$130,000 partner and white label. It steps once, on 1 January 2028, and a firm keeps what it signed at.
2031	\$105,276,946 of total revenue, \$108,935,933 of recurring revenue at 31 December, 835 end customers and 31 partners, 47 employees against 79 contracted full time equivalents, 77.6 per cent gross margin.
The market	\$840,471,950 of recurring market at the card, \$490,572,719 budget qualified, and \$72,179,000 at the 745 alone. The fully penetrated ceiling of \$1,770,732,455 is a ceiling and is never a denominator.
Capital	\$2,050,000 of pre-seed across five instalments, then \$3,500,000 of seed in Q4 2028 at \$30,000,000 post-money. A \$500,000 borrowing facility at 8 per cent, switched off, so every figure above is share money alone.
The road	Eight overdrawn months, lowest May 2028 at \$778,960 short. Runway of 1.06 months at the seed decision against a twelve month threshold the plan sets itself. Both read REVIEW on the workbook's own checks.
What is held out on purpose	Consumer driven banking, 578 entities at zero revenue. Payment providers in review, 459, outside the denominator. Both because no register of approved firms exists.
What must not be quoted	The earnings margin. The workbook's check on it reads REVIEW because the cost base has not been rebuilt for six revenue lines, and it says so.

SOURCES ON THIS PAGE

The register and the card	Bank of Canada registry data feed · public registry · about 1,600 providers, in the Bank's own words · the daily rate of 14 August 2026 . Card and market from 4orm Finance Price Evidence, all tiers, 17 August 2026 and 4orm Finance master pro forma rebuild of 16 August 2026, base case, recalculated in full.	PRIMARY / MODEL
Every other figure	4orm Finance master pro forma rebuild of 16 August 2026, base case, recalculated in full. 4orm Finance Master Source Register, 16 August 2026, 162 rows and 162 external sources, every one live. 4orm Finance Vision, 17 August 2026.	MODEL
